

| Activity ID | Activity Description | Orig Dur | Early Start | Early Finish | 2009 | | | | | | | | | | | | | | | | | | | | | | | | | | | |
|-------------|----------------------|----------|-------------|--------------|------|---|----|----|----|-----|----|----|----|-----|---|----|----|-----|---|----|----|-----|---|----|----|----|---|--|--|--|--|--|
| | | | | | 2008 | | | | | JAN | | | | FEB | | | | MAR | | | | APR | | | | M | | | | | | |
| | | | | | 1 | 8 | 15 | 22 | 29 | 5 | 12 | 19 | 26 | 2 | 9 | 16 | 23 | 2 | 9 | 16 | 23 | 30 | 6 | 13 | 20 | 27 | 4 | | | | | |


| Project Administration | | | | |
|------------------------|-------------------------|-----|----------|---------|
| 1000 | Notice of Award | 1 | 05DEC08* | 05DEC08 |
| 1032 | Preconstructoin Meeting | 1 | 11DEC08 | 11DEC08 |
| 1030 | Contract Duration | 108 | 12DEC08 | 29MAR09 |

| Mobilization | | | | |
|--------------|-------------------|---|---------|---------|
| 1040 | Saltaire Pipeline | 4 | 27DEC08 | 30DEC08 |
| 1065 | Beach Equipment | 3 | 27DEC08 | 29DEC08 |
| 1050 | 1st Dredge Mob | 1 | 31DEC08 | 31DEC08 |
| 1055 | 2nd Dredge Mob | 1 | 01FEB09 | 01FEB09 |

| Surveying | | | | |
|-----------|--|---|---------|---------|
| 1060 | Saltaire B.D.s & Structure Survey | 4 | 19DEC08 | 22DEC08 |
| 1070 | Fire Island Pines B.D.s & Structure Survey | 4 | 29JAN09 | 01FEB09 |
| 1080 | Saltaire A.D.s | 4 | 02FEB09 | 05FEB09 |
| 1090 | Ocean Beach B.D.s & Structure Survey | 4 | 18FEB09 | 21FEB09 |
| 1075 | Fire Island Pines A.D.s | 4 | 22FEB09 | 25FEB09 |
| 1085 | Davis Park B.D.s & Structure Survey | 4 | 11MAR09 | 14MAR09 |
| 1095 | Ocean Beach A.D.s | 4 | 15MAR09 | 18MAR09 |
| 1105 | Davis Park A.D.s | 4 | 27MAR09 | 30MAR09 |

| Dredging | | | | |
|----------|-------------------|----|---------|---------|
| 1190 | Saltaire | 32 | 01JAN09 | 01FEB09 |
| 1194 | Fire Island Pines | 21 | 02FEB09 | 22FEB09 |
| 1204 | Ocean Beach | 20 | 22FEB09 | 13MAR09 |
| 1214 | Davis Park | 12 | 15MAR09 | 26MAR09 |

| Demobilization | | | | |
|----------------|-----------------|---|---------|---------|
| 1300 | Beach Equipment | 3 | 27MAR09 | 29MAR09 |

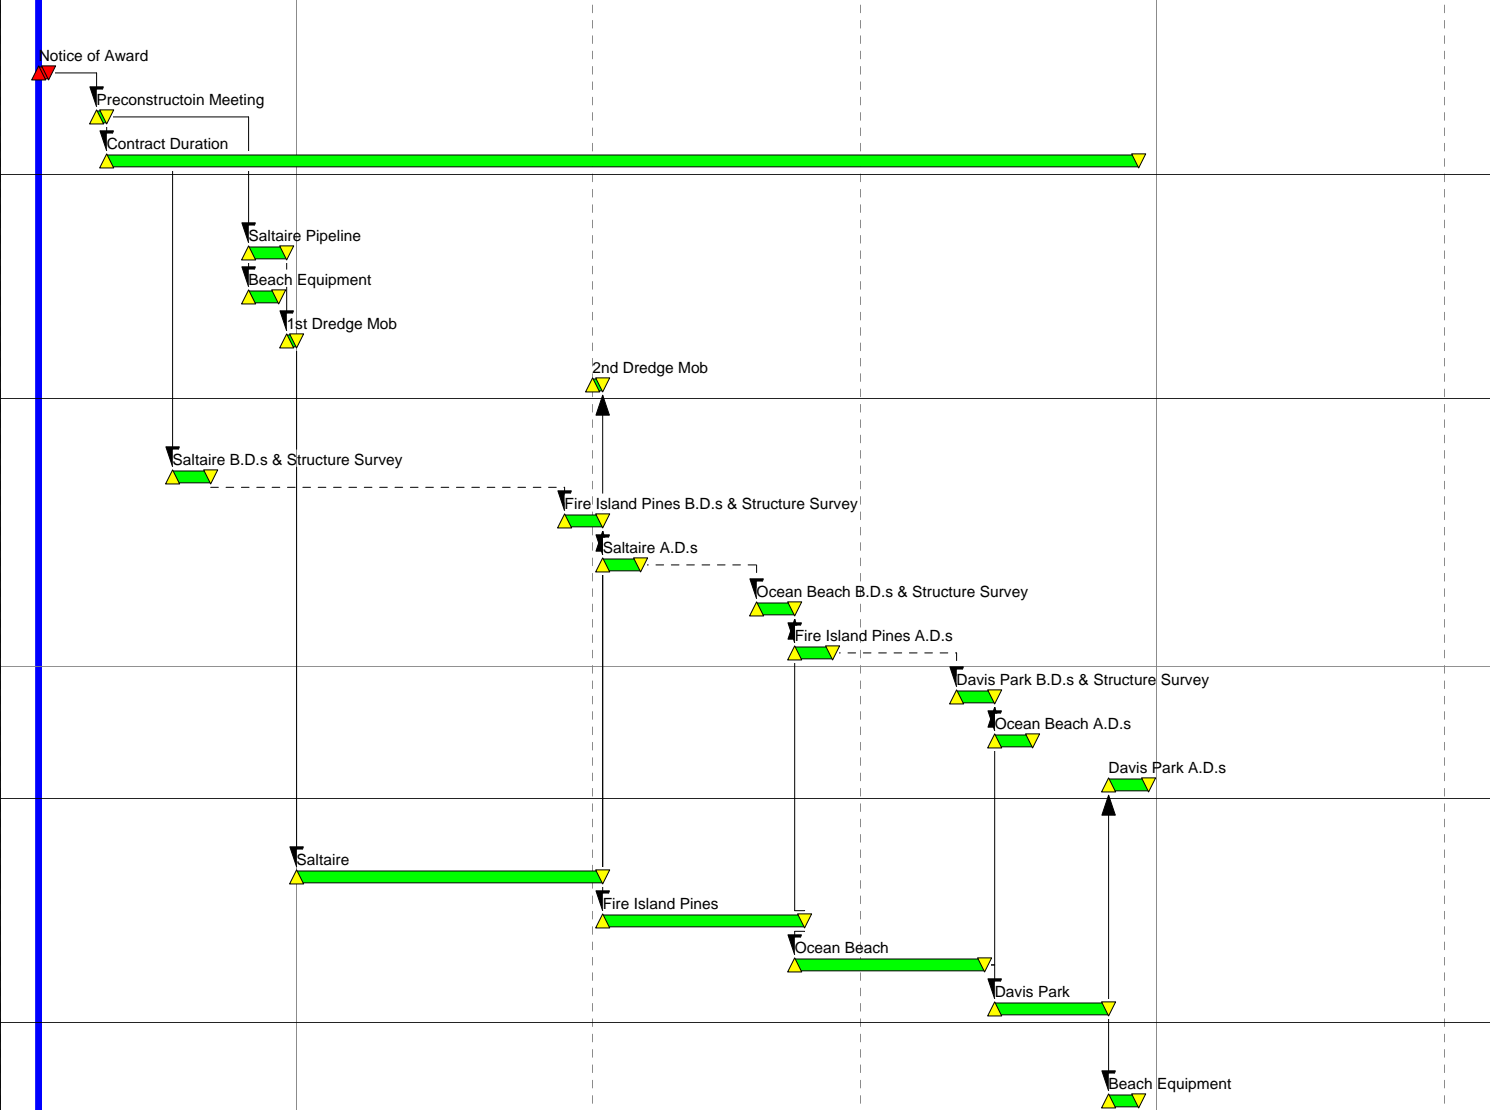

| | | | |
|-------------|---------------|--|-------------------|
| Start Date | 01DEC08 | | Early Bar |
| Finish Date | 30MAR09 | | Progress Bar |
| Data Date | 05DEC08 | | Critical Activity |
| Run Date | 11DEC08 09:47 | | |

Weeks Marine, Inc
Fire Island Beaches
